

**CHANGE TO CONTRACT  
CHANGE ORDER NUMBER 2  
2015 STREET IMPROVEMENTS PROJECT  
THIRD AVENUE NW FROM FIRST STREET NW TO THIRD STREET NW  
FIFTH AVENUE NW FROM FIRST STREET NW TO SEVENTH STREET NW**

**September 4, 2015**

**OWNER: CITY OF MOUNT VERNON, IOWA  
CONTRACTOR: RICKLEFS EXCAVATING, ANAMOSA, IOWA**

ITEM 1: The total scope of the Third Avenue paving was shortened, the pavement section was changed to full depth Portland Cement Concrete with a drainable sub base, and the existing sub grade was found to be unstable and needed to be stabilized. For these reasons it was determined by the Engineer that drain tile may now be necessary at the intersection of Third Avenue and Third Street. The Contractor was asked for a price to install sub drain under the proposed pavement and the proposed price was reviewed and agreed upon by the city Administrator. Although the subdrain does not out fall now, it provides for a future connection without the need to remove new pavement.

**ADDITIONAL PRICE TO CONTRACT: \$ 2,994.00**

ADDITIONAL CONTRACT TIME None

**CONTRACT SUMMARY:**

CONTRACT PRICE	\$ 902,281.35
CHANGE ORDER 1	\$ 10,260.00
CHANGE ORDER 2	<u>\$ 2,994.00</u>
REVISED CONTRACT PRICE	\$ 915,535.35

Ricklefs Excavating

By: \_\_\_\_\_

Title: \_\_\_\_\_

Date: \_\_\_\_\_

City of Mt. Vernon, Iowa

City of Mt. Vernon, Iowa

\_\_\_\_\_  
City Engineer

\_\_\_\_\_  
City Administrator

Date: \_\_\_\_\_

Date: \_\_\_\_\_

# RICKLEFS EXCAVATING, LTD

# Request for Change

12536 Buffalo Road  
Anamosa, IA 52205

RFC Number: 2  
Date: 09/03/2015

**Regarding:**

To provide payment for the added 6 inch drain tile and cleanouts in the 3rd Ave and 3rd St intersection as requested.

**To:**

City of Mount Vernon  
213 First Street West  
Mount Vernon, IA 52314

**Job Site:**

Mount Vernon 2015 Street Imp.  
213 First Street West  
Mount Vernon, IA 52314

**Requested By:**

Cory Elwick

**Phone:**

(319) 462-4435

**E-mail:**

corye@ricklefsexcavating.com

**Recipients:**

Dan Boggs

**Phone:**

(319) 350-2473

**E-mail:**

dboggs@cityofmtvernonia.gov

**Requested Change:**

Requested Change:	U/M	Qty	Unit Price	Change to Contract
6" Drain Tile Supplied & Installed	L.F.	141.000000	15.000000	2115.00
		0		
Clean Outs Supplied & Installed	EA	3.000000	293.000000	879.00


**RFC Total**

**\$ 2994.00**

Please respond by: 09/04/2015

Cory Elwick  
Ricklefs Excavating, Ltd

Dan Boggs  
City of Mount Vernon

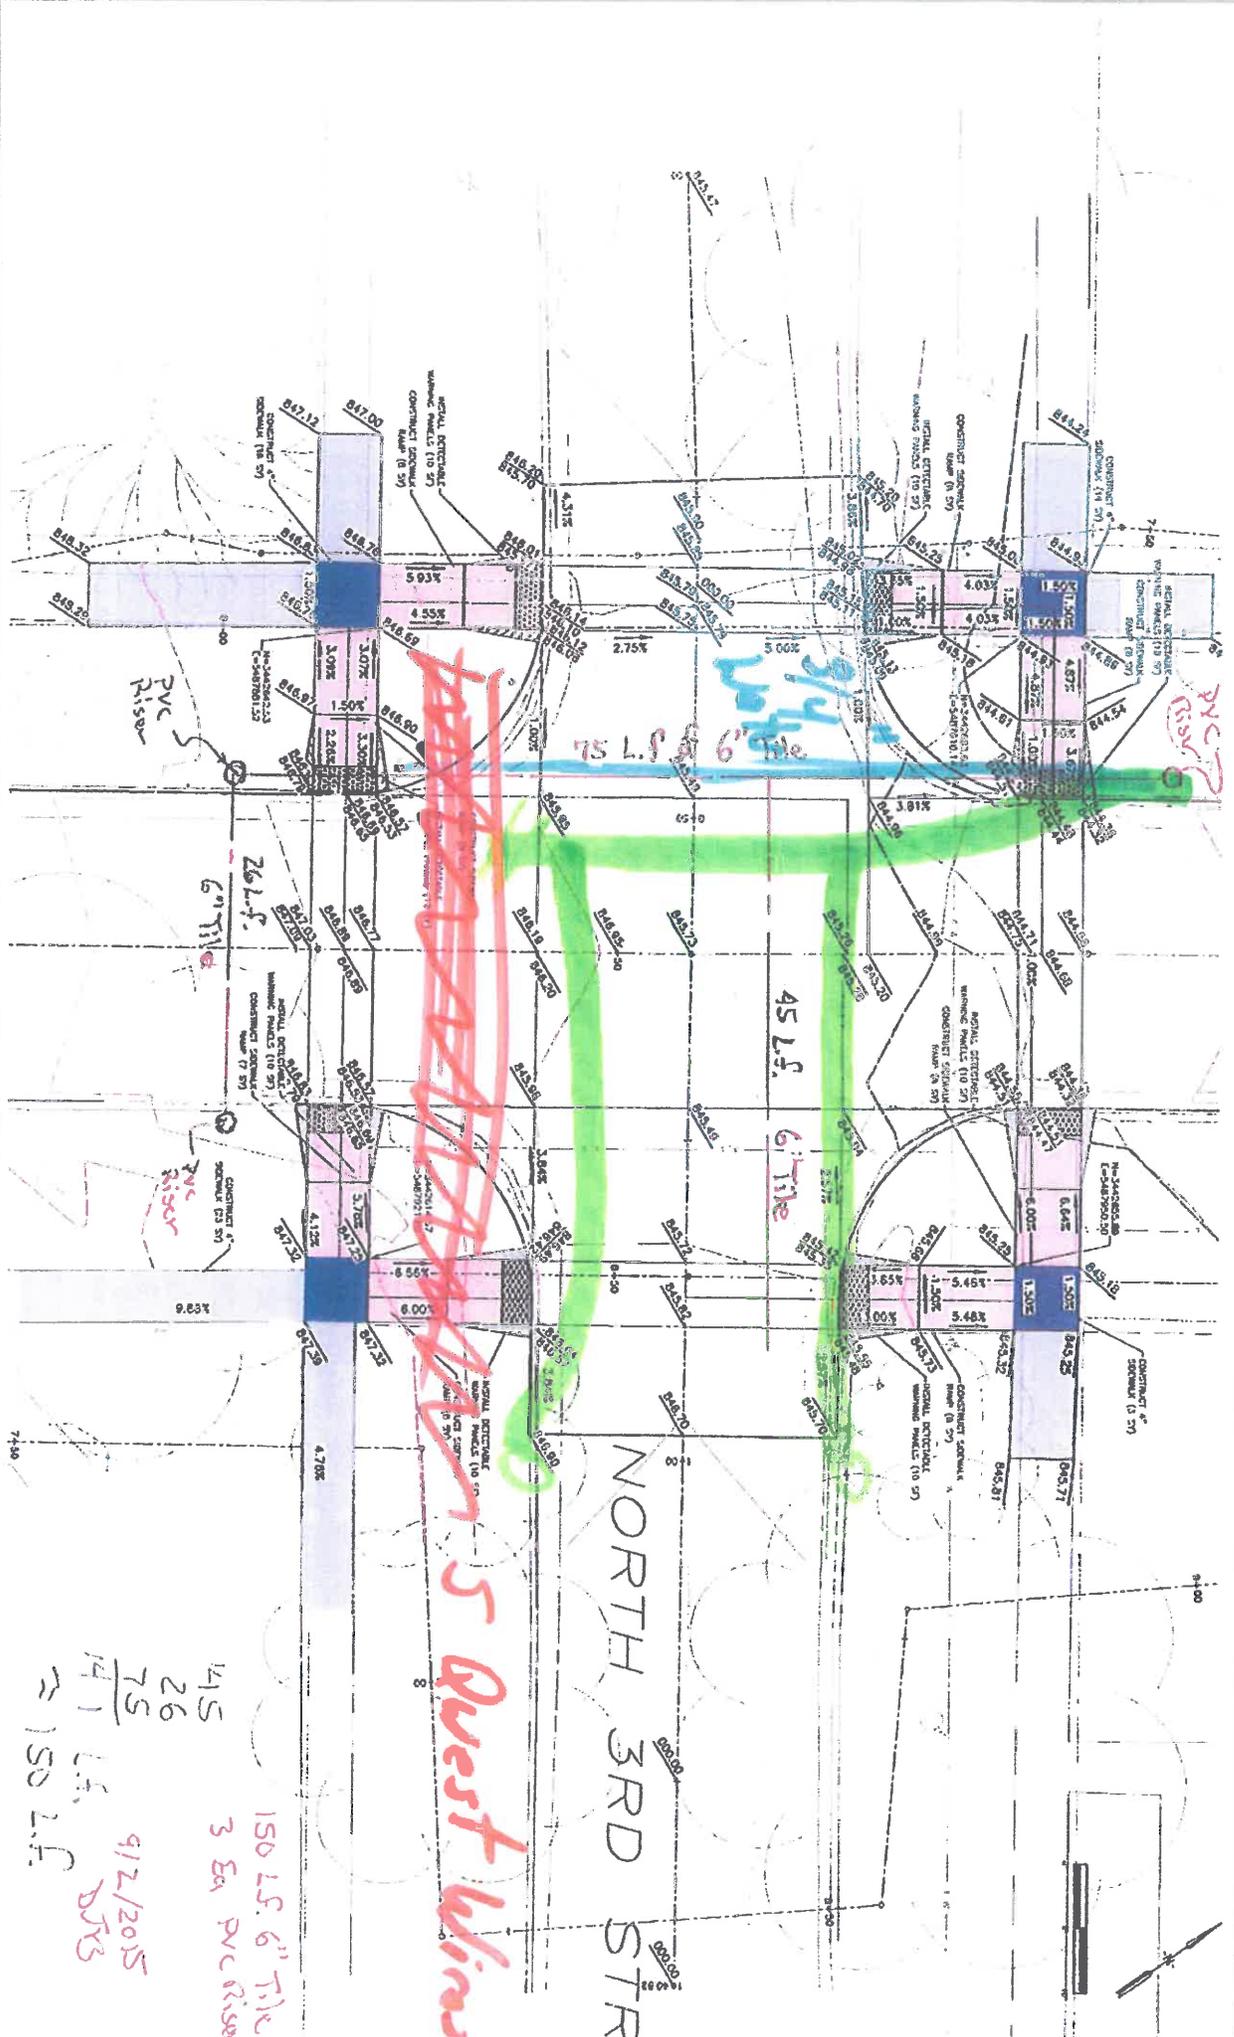

145  
26  
75  
141 L.F.  
9/2/2015  
DJB

150 L.F. 6" Tile  
3 Ea PVC Risers

~~XXXXXXXXXXXXXXXXXXXX~~ 5 Quest Lines

DATE	REVISIONS	SCALE	VERTICAL SCALE
	1. AS SHOWN	AS SHOWN	AS SHOWN
	2. AS SHOWN	AS SHOWN	AS SHOWN
	3. AS SHOWN	AS SHOWN	AS SHOWN
	4. AS SHOWN	AS SHOWN	AS SHOWN
	5. AS SHOWN	AS SHOWN	AS SHOWN
	6. AS SHOWN	AS SHOWN	AS SHOWN
	7. AS SHOWN	AS SHOWN	AS SHOWN
	8. AS SHOWN	AS SHOWN	AS SHOWN
	9. AS SHOWN	AS SHOWN	AS SHOWN
	10. AS SHOWN	AS SHOWN	AS SHOWN
	11. AS SHOWN	AS SHOWN	AS SHOWN
	12. AS SHOWN	AS SHOWN	AS SHOWN
	13. AS SHOWN	AS SHOWN	AS SHOWN
	14. AS SHOWN	AS SHOWN	AS SHOWN
	15. AS SHOWN	AS SHOWN	AS SHOWN
	16. AS SHOWN	AS SHOWN	AS SHOWN
	17. AS SHOWN	AS SHOWN	AS SHOWN
	18. AS SHOWN	AS SHOWN	AS SHOWN
	19. AS SHOWN	AS SHOWN	AS SHOWN
	20. AS SHOWN	AS SHOWN	AS SHOWN
	21. AS SHOWN	AS SHOWN	AS SHOWN
	22. AS SHOWN	AS SHOWN	AS SHOWN
	23. AS SHOWN	AS SHOWN	AS SHOWN
	24. AS SHOWN	AS SHOWN	AS SHOWN
	25. AS SHOWN	AS SHOWN	AS SHOWN
	26. AS SHOWN	AS SHOWN	AS SHOWN
	27. AS SHOWN	AS SHOWN	AS SHOWN
	28. AS SHOWN	AS SHOWN	AS SHOWN
	29. AS SHOWN	AS SHOWN	AS SHOWN
	30. AS SHOWN	AS SHOWN	AS SHOWN
	31. AS SHOWN	AS SHOWN	AS SHOWN
	32. AS SHOWN	AS SHOWN	AS SHOWN
	33. AS SHOWN	AS SHOWN	AS SHOWN
	34. AS SHOWN	AS SHOWN	AS SHOWN
	35. AS SHOWN	AS SHOWN	AS SHOWN
	36. AS SHOWN	AS SHOWN	AS SHOWN
	37. AS SHOWN	AS SHOWN	AS SHOWN
	38. AS SHOWN	AS SHOWN	AS SHOWN
	39. AS SHOWN	AS SHOWN	AS SHOWN
	40. AS SHOWN	AS SHOWN	AS SHOWN
	41. AS SHOWN	AS SHOWN	AS SHOWN
	42. AS SHOWN	AS SHOWN	AS SHOWN
	43. AS SHOWN	AS SHOWN	AS SHOWN
	44. AS SHOWN	AS SHOWN	AS SHOWN
	45. AS SHOWN	AS SHOWN	AS SHOWN
	46. AS SHOWN	AS SHOWN	AS SHOWN
	47. AS SHOWN	AS SHOWN	AS SHOWN
	48. AS SHOWN	AS SHOWN	AS SHOWN
	49. AS SHOWN	AS SHOWN	AS SHOWN
	50. AS SHOWN	AS SHOWN	AS SHOWN
	51. AS SHOWN	AS SHOWN	AS SHOWN
	52. AS SHOWN	AS SHOWN	AS SHOWN
	53. AS SHOWN	AS SHOWN	AS SHOWN
	54. AS SHOWN	AS SHOWN	AS SHOWN
	55. AS SHOWN	AS SHOWN	AS SHOWN
	56. AS SHOWN	AS SHOWN	AS SHOWN
	57. AS SHOWN	AS SHOWN	AS SHOWN
	58. AS SHOWN	AS SHOWN	AS SHOWN
	59. AS SHOWN	AS SHOWN	AS SHOWN
	60. AS SHOWN	AS SHOWN	AS SHOWN
	61. AS SHOWN	AS SHOWN	AS SHOWN
	62. AS SHOWN	AS SHOWN	AS SHOWN
	63. AS SHOWN	AS SHOWN	AS SHOWN
	64. AS SHOWN	AS SHOWN	AS SHOWN
	65. AS SHOWN	AS SHOWN	AS SHOWN
	66. AS SHOWN	AS SHOWN	AS SHOWN
	67. AS SHOWN	AS SHOWN	AS SHOWN
	68. AS SHOWN	AS SHOWN	AS SHOWN
	69. AS SHOWN	AS SHOWN	AS SHOWN
	70. AS SHOWN	AS SHOWN	AS SHOWN
	71. AS SHOWN	AS SHOWN	AS SHOWN
	72. AS SHOWN	AS SHOWN	AS SHOWN
	73. AS SHOWN	AS SHOWN	AS SHOWN
	74. AS SHOWN	AS SHOWN	AS SHOWN
	75. AS SHOWN	AS SHOWN	AS SHOWN
	76. AS SHOWN	AS SHOWN	AS SHOWN
	77. AS SHOWN	AS SHOWN	AS SHOWN
	78. AS SHOWN	AS SHOWN	AS SHOWN
	79. AS SHOWN	AS SHOWN	AS SHOWN
	80. AS SHOWN	AS SHOWN	AS SHOWN
	81. AS SHOWN	AS SHOWN	AS SHOWN
	82. AS SHOWN	AS SHOWN	AS SHOWN
	83. AS SHOWN	AS SHOWN	AS SHOWN
	84. AS SHOWN	AS SHOWN	AS SHOWN
	85. AS SHOWN	AS SHOWN	AS SHOWN
	86. AS SHOWN	AS SHOWN	AS SHOWN
	87. AS SHOWN	AS SHOWN	AS SHOWN
	88. AS SHOWN	AS SHOWN	AS SHOWN
	89. AS SHOWN	AS SHOWN	AS SHOWN
	90. AS SHOWN	AS SHOWN	AS SHOWN
	91. AS SHOWN	AS SHOWN	AS SHOWN
	92. AS SHOWN	AS SHOWN	AS SHOWN
	93. AS SHOWN	AS SHOWN	AS SHOWN
	94. AS SHOWN	AS SHOWN	AS SHOWN
	95. AS SHOWN	AS SHOWN	AS SHOWN
	96. AS SHOWN	AS SHOWN	AS SHOWN
	97. AS SHOWN	AS SHOWN	AS SHOWN
	98. AS SHOWN	AS SHOWN	AS SHOWN
	99. AS SHOWN	AS SHOWN	AS SHOWN
	100. AS SHOWN	AS SHOWN	AS SHOWN

2015 STREET IMPROVEMENTS  
CITY OF MOUNT VERNON  
3RD AVE INTERSECTIONS - 3RD ST NW

VENUSTRA & KIMM, INC.

840 2nd Avenue • Suite 4 • Cascade, WA 98241-1533  
317-644-1000 • J17@kimm.com • 509-241-0001/VW15

DATE: L.04
